

Work Order ID 145736

Friday, May 06, 2016 10:44:26 AM

145736

Page 1

Item ID: D4271-025

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: End Fitting Assembly Fwd Beam

Start Date: 5/3/2016 Start Qty: 2.00

2
2

Cust Item ID:

Required Date: 5/5/2016 Req'd Qty: 2.00

Customer:

Reference:

Approvals:

Process Plan: dmDate: 16/05/09

Tooling:

Date:

QC:

Date:

SPC (Y/N):

Date:

Run Start ***NR1***Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D4271	D

100

100

Small Fab

Small Fab

Memo

Assemble as per dwg D4271
REAM HOLE AS PER DWG
CUT RIVET AT 1.130"
C' SINK AT .220" X100 DEG FOR HOLE OPPOSITE TO HEAD

0.00

0.80

110

110

QC

Quality Control

QC5- Inspect part completeness to step on W/O

Memo

0.00

0.04

120

120

Packaging

Packaging

Identify as per dwg & Stock Location: S1370

Memo

0.00

0.02

SEP 07 2016

2x

16/09/14

(2)

SEP 16 2016

2 DAS 6 9-89

SEP 15 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																													
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval																																																									
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval																																																									
Root Cause		FAULT CATEGORY																																																															
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____			
Misidentified ☐	Past Due ☐																																																																

Work Order ID 145736

Friday, May 06, 2016 10:44:26 AM

145736

Page 2

Item ID: D4271-025 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: End Fitting Assembly Fwd Beam
Start Date: 5/3/2016 Start Qty: 2.00 ***2*** Cust Item ID:
Required Date: 5/5/2016 Req'd Qty: 2.00 ***2*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
130	QC21- Final Inspection - Work Order Release	0.00							
130									
QC	Memo	0.20							
Quality Control									

MLJ 16-07-15
MLJ 16-07-15

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition			
				Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					

Picklist Print

Friday, May 06, 2016 10:44:25 AM

Page 1
13

Work Order ID: 145736

145736

Parent Item: D4271-025

D4271-025

Parent Item Name: End Fitting Assembly Fwd Beam

Start Date: 5/3/2016

Required Date: 5/5/2016

Start Qty: 2.00

Required Qty: 2.00

Comments: IPP revA 11.07.20 new issue EC veriufied by:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D4149-5 *D4149-5* Eyebolt Stud		Manufactured	No			100	Each	9.0000	1	21 143649			DAS 6 9-89
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			
				ST086				9					
					143341			9					
D4419-1 *D4419-1* Fwd Support Plate		Manufactured	No			100	Each	7.0000	2	4 145844			DAS 6 9-89
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			
				ST097				7					
					123027			7					
D4281-1 *D4281-1* Spacer		Manufactured	No			100	Each	5.0000	1	21			DAS 6 9-89
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			
				ST090				5					
					117102			5					
D4281-3 *D4281-3* Spacer		Manufactured	No			100	Each	4.0000	1	2 145996			DAS 6 9-89
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			
				ST090				4					
					123097			4					

SEP 07 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐		OTHER : ☐					

Picklist Print

Friday, May 06, 2016 10:44:25 AM

Page 2

Work Order ID: 145736

145736

Parent Item: D4271-025

D4271-025

Parent Item Name: End Fitting Assembly Fwd Beam

Start Date: 5/3/2016

Required Date: 5/5/2016

Start Qty: 2.00

Required Qty: 2.00

AN4C13A Purchased No

100 Each 133.0000 2 4

AN4C13A
BOLT

**

134.50

DAS
6
9-89

Location

Loc Qty

Loc Code

OVER002

50

m134508

50

over003

50

m134497

50

ST344

33

m134365

3

m134573

30

4

MS20427M4-20 Purchased No

100 Each 93.0000 1 2

MS20427M4-20
RIVET

**

DAS
6
9-89

Location

Loc Qty

Loc Code

GA

93

118429

93

2

MS20615-4M18 Purchased No

100 Each 223.0000 10 20

MS20615-4M18
Rivet

**

DAS
6
9-89

Location

Loc Qty

Loc Code

OVER007

100

m134502

50

m134606

50

ST306

123

m134134

23

m134370

50

m134676

50

20

SEP 07 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval 	
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	

Root Cause				FAULT CATEGORY			
Environment ☐	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐
Design ☐	☐	Operator	☐	Bending	☐	Set-up	☐
Doc/Data ☐	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐
Equip/Tooling ☐	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐
Handling/Pre ☐	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐
Material ☐	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐
Internal Transport ☐	☐	Poor Information	☐	Crushing	☐	Countersink	☐
Tribal Knowledge ☐	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐
LOA ☐	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐
Substation ☐	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐
Past Expiry Date ☐	☐	Manufacturing Process	☐	OTHER : _____			
Misidentified ☐	☐	Past Due	☐				

Picklist Print

Friday, May 06, 2016 10:44:25 AM

Page 3

Work Order ID: 145736

145736

Parent Item: D4271-025

D4271-025

Parent Item Name: End Fitting Assembly Fwd Beam

Start Date: 5/3/2016

Required Date: 5/5/2016

Start Qty: 2.00

Required Qty: 2.00

MS21043-4

Purchased

No

100

Each

889.0000

2

4

MS21043-4

Nut

135390

DAS
6
9-89

Location

Loc Qty

Loc Code

FG

40

104603

40

GA

95

m132803

95

OVER007

300

m134502

300

ST302

454

m133769

12

m134249

142

m134634

300

NAS1149C0432R

Purchased

No

100

Each

1,857.000

4

8

NAS1149C0432R

WASHER

135297

DAS
6
9-89

Location

Loc Qty

Loc Code

GA

428

m125807

428

ST266

1429

m134073

429

m134676

1000

SEP 07 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE


QA Closed: _____ Date: _____

Work Order update only ☐


Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval 	
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	

Root Cause				FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER : _____							
Misidentified	☐	Past Due	☐								

ITEM	QTY -011	QTY -013	P/N	DESCRIPTION
	X		D4271-011	FWD BEAM ASSEMBLY
		X	D4271-013	AFT BEAM ASSEMBLY
	-	-	D4271-021	DELETED AT REVISION D
	-	-	D4271-023	DELETED AT REVISION D
1	1	-	D4271-025	FWD BEAM END FITTING ASSEMBLY
2	-	1	D4271-027	AFT BEAM END FITTING ASSEMBLY
3	1	-	D4275-1	FWD BEAM
4	-	1	D4276-1	AFT BEAM
5	6	6	AN3C12A	BOLT
6	6	6	MS21043-3	NUT
7	12	12	NAS1149C0332R	WASHER

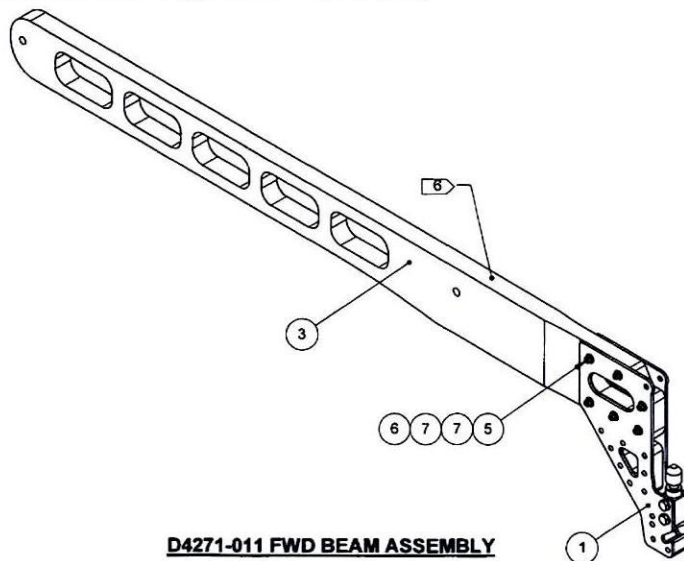

D4271-011 FWD BEAM ASSEMBLY

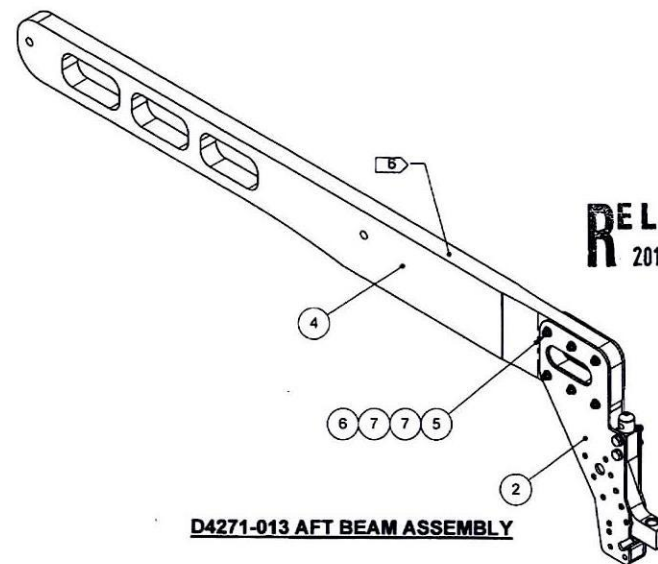

D4271-013 AFT BEAM ASSEMBLY

RELEASED
2011-07-28

NOTES:


- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY WITH DART IDENTIFY WITH DART P/N "D4271-0XX" AND B/N "BXXXXX" PER DART QSI 044 6.1 (FINE POINT MARKER)
- 7) WEIGHT -011: 11.02 lbs
-013: 12.97 lbs

D	DELETED -021 & -023 REPLACED BY -025 & -027 FOR Q.R. STEP INSTALLATION.	AJS	11.07.14
C	ADDED -021 & -023 FOR EASE OF CONFIGURATION MANAGEMENT. REFORMAT SEE PREV REV FOR DETAILS.	AJS	11.07.12
B	ITEM 10 CHANGED FROM AN3C12A TO AN4C13A	SC	10.12.01
A	NEW ISSUE	SC	10.11.25
REV.	DESCRIPTION	BY	DATE
DESIGN	JPH	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AJS		
CHECKED	<i>[Signature]</i>	DRAWING NO.	REV. D
MFG. APPR.	<i>[Signature]</i>	D4271	SHEET 1 OF 3
APPROVED	<i>[Signature]</i>	TITLE	SCALE
DE APPR.	<i>[Signature]</i>	SUPPORT BEAM ASSEMBLIES	NTS
DATE	11.07.14	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

w/o 145736

dm 16/05/09



ITEM	QTY -025	P/N	DESCRIPTION
	X	D4271-025	FWD BEAM END FITTING ASSEMBLY
1	1	D4149-5	EYEBOLT STUD
3	1	D4281-1	SPACER
4	1	D4281-3	SPACER
5	2	D4419-1	FWD SUPPORT PLATE
6	2	AN4C13A	BOLT
7	1	MS20427M4-20	CSK RIVET (MONEL)
8	10	MS20615-4M18	RIVET (MONEL)
9	2	MS21043-4	NUT
10	4	NAS1149C0432R	WASHER

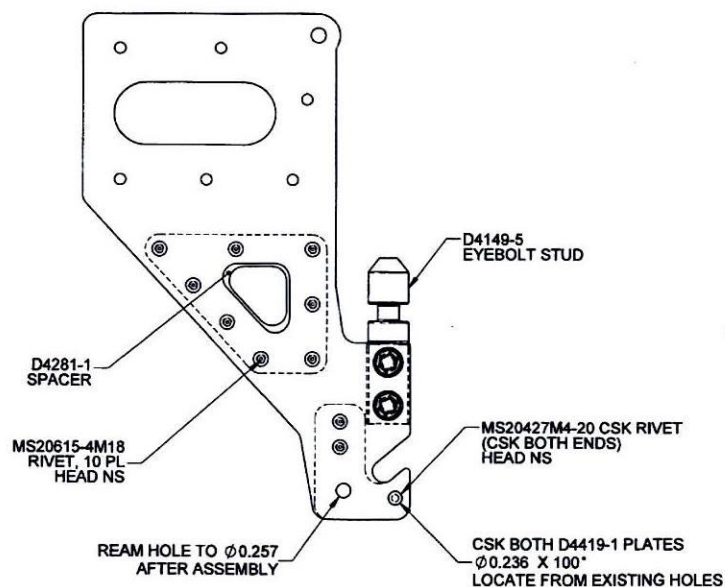

D4271-025 FWD BEAM END FITTING ASSEMBLY

NOTES:


- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY WITH DART IDENTIFY WITH DART P/N "D4271-025" AND B/N "BXXXXX" PER DART QSI 044 6.1 (FINE POINT MARKER)
- 7) WEIGHT: 2.69 lbs

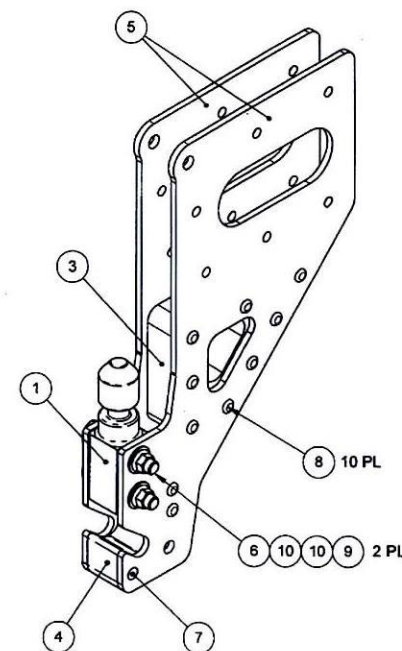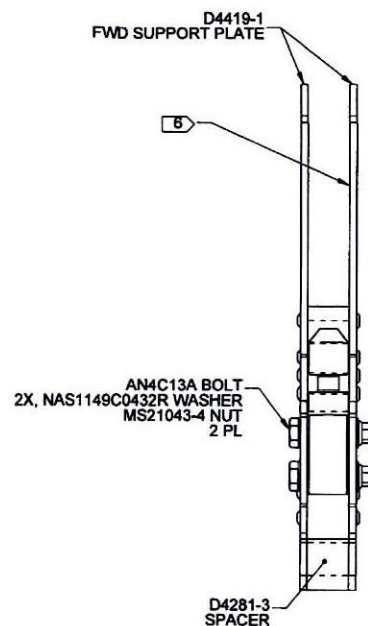

RELEASED
2011-07-28

DESIGN	JPH	DART AEROSPACE LTD	
DRAWN	AJS	HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. D
MFG. APPR.		D4271	SHEET 2 OF 3
APPROVED		TITLE	SCALE
DE APPR.		SUPPORT BEAM ASSEMBLIES	NTS
DATE	11.07.14	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD	



ITEM	QTY -027	P/N	DESCRIPTION
	X	D4271-027	AFT BEAM END FITTING ASSEMBLY
1	1	D4148-3	STUD RECEIVER LOWER
2	1	D4148-5	EYEBOLT STUD
3	1	D4281-3	SPACER
4	2	D4419-3	AFT SUPPORT PLATE
5	2	AN4C13A	BOLT
6	1	MS20427M4-20	CSK RIVET (MONEL)
7	10	MS20615-4M18	RIVET (MONEL)
8	2	MS21043-4	NUT
9	4	NAS1149C0432R	WASHER

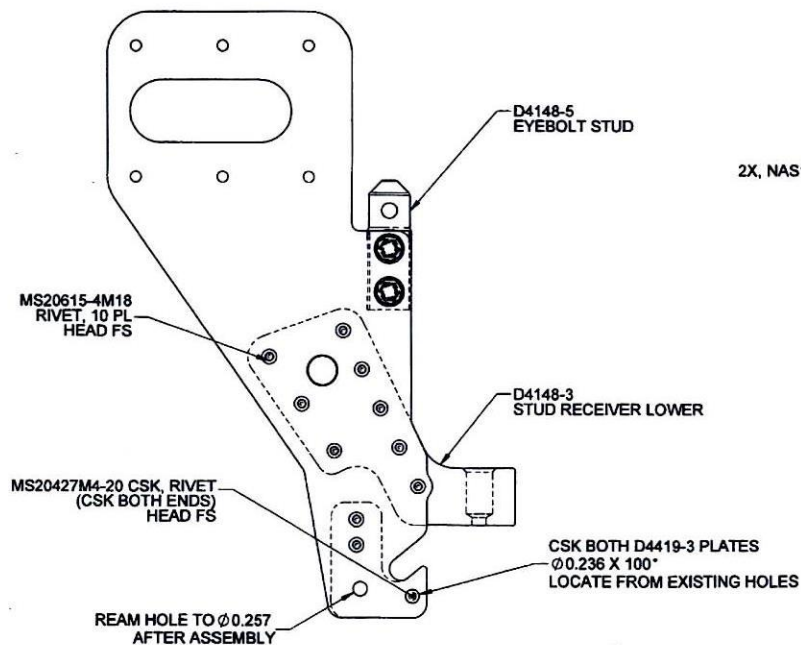

D4271-027 AFT BEAM END FITTING ASSEMBLY

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY WITH DART IDENTIFY WITH DART P/N "D4271-027" AND B/N "BXXXXX" PER DART QSI 044 6.1 (FINE POINT MARKER)
- 7) WEIGHT: 4.25 lbs

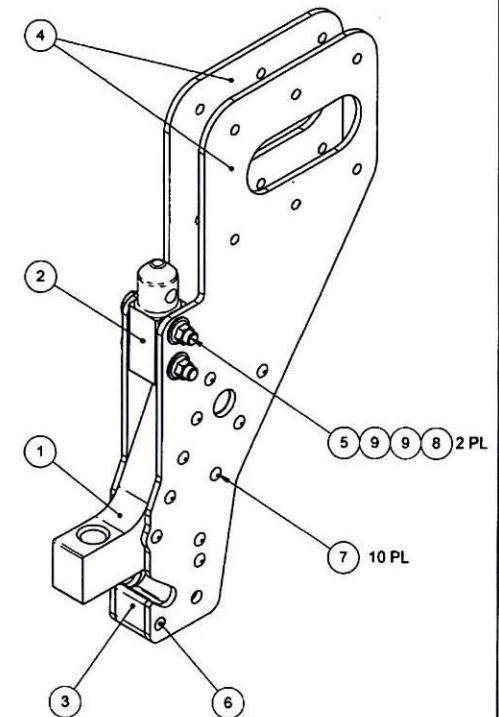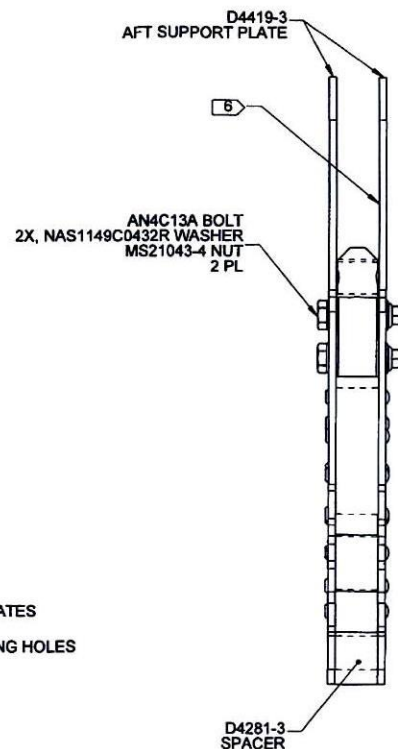

RELEASED
2011-07-28

DESIGN	JPH	DART AEROSPACE LTD	
DRAWN	AJS	HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. D
MFG. APPR.		D4271	SHEET 3 OF 3
APPROVED		TITLE	SCALE
DE APPR.		SUPPORT BEAM ASSEMBLIES	NTS
DATE	11.07.14	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
